

SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura ICF to the new fourth-floor storey only - 6in XR35 external walls + 6in Standard stair-core and separating walls, 7 courses on the steel ring beam - pre-cut by BuildEase, stock forms and accessories by the distributor. The existing building, steelwork, floor, roof, partitions and finishes are shown or assumed in good faith only and must be checked by the relevant professional; the structural engineer to design the ring beam, transfer steels and the walls.

QUOTATION - NOT FOR CONSTRUCTION

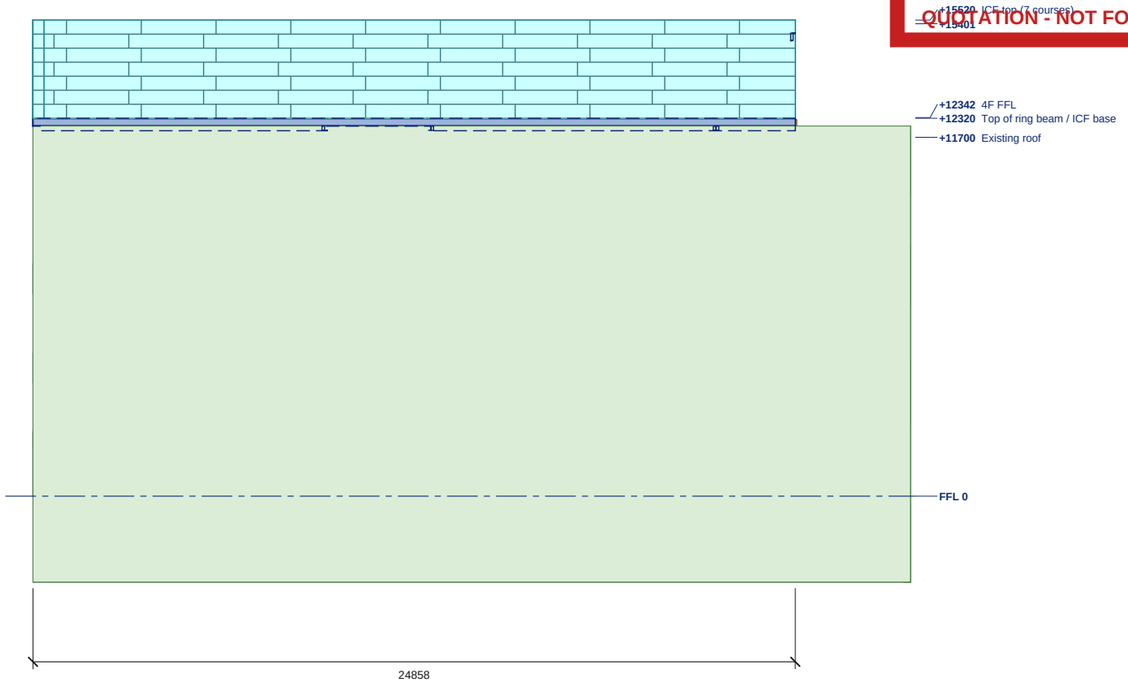

SIDE (WEST) ELEVA

Scale 1:200 @ A3 | Levels ab

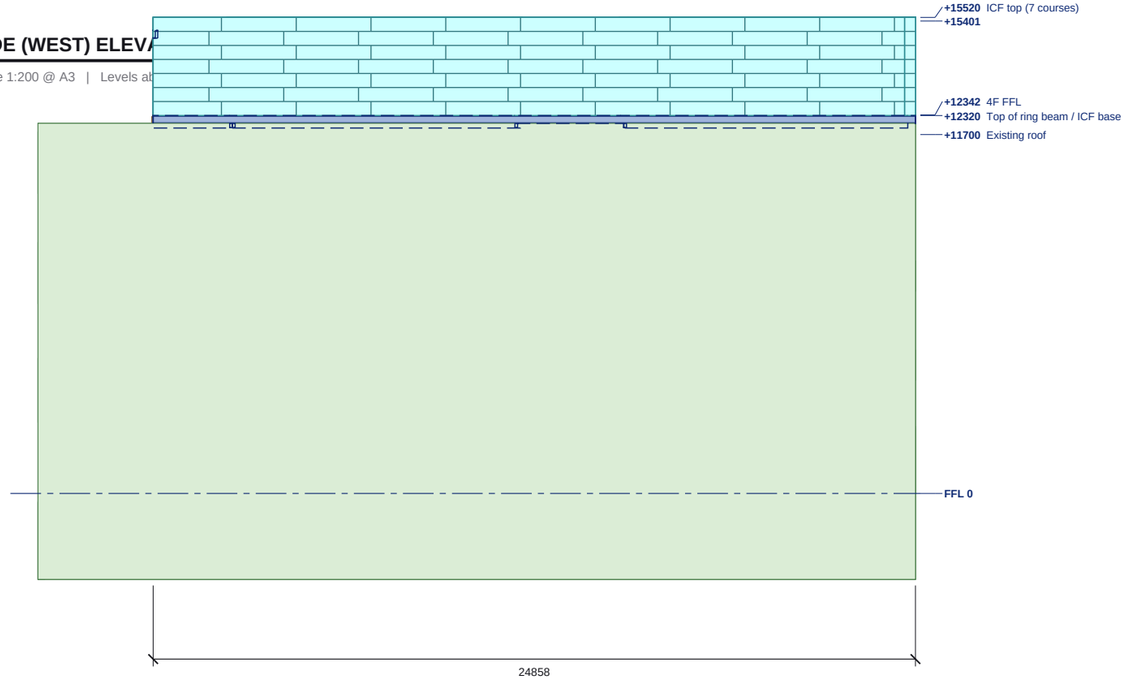

SIDE (EAST) ELEVATION

Scale 1:200 @ A3 | Levels above GF FFL; sills and heads in the schedule



Do not scale. All dimensions in millimetres; levels in metres from GF FFL. Check all dimensions on site.

ELEVATION SCHEDULES

SIDE (WEST) ELEVATION - NEIGHBOUR: OPENINGS

Ref	Width	Height	Sill	Head	Lintel
none					

Structural openings in the ICF; sill and head above GF FFL.

SIDE (EAST) ELEVATION: OPENINGS

Ref	Width	Height	Sill	Head	Lintel
none					

Structural openings in the ICF; sill and head above GF FFL.

SIDE (WEST) ELEVATION - NEIGHBOUR: LEVELS

Level	FFL
GF FFL	0
Existing roof	+11700
Top of ring beam / ICF base	+12320
4F FFL	+12342
top of roof build-up	+15401
ICF top (7 courses)	+15520

SIDE (EAST) ELEVATION: LEVELS

Level	FFL
GF FFL	0
Existing roof	+11700
Top of ring beam / ICF base	+12320
4F FFL	+12342
top of roof build-up	+15401
ICF top (7 courses)	+15520

NOTES

1. ICF: Nudura 6" XR35, 101.6 EPS + 152.4 core + 101.6 EPS = 355.6; 6" Std, 66.7 EPS + 152.4 core + 66.7 EPS = 285.8. External EPS face shown with the block course joints, vertical block joints and stack joints as populated.
2. Levels above GF FFL. Openings are structural openings in the ICF; glazing, doors, render and finishes by others, not shown.
3. Steel and masonry shown as modelled.
4. See ES26-055-GA-01 for plan setting out, lintels and steel.
5. Datum: 0 = rear yard ground (~ +14.92 AOD). ICF base = top of steel ring beam +12,320 (~ +27.24 AOD).
6. From Huw Griffiths Architects HG-24-02-02/03/05/06 (Planning) and JVS roof survey 041/24.
7. Existing building, steel ring beam / transfer steels, floor and roof structure shown indicatively only.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
Insubloc (distributor) - Tim Evans	2 Castle Gardens, Swansea - new fourth-floor storey (4 flats)

DRAWING TITLE

SIDE ELEVATIONS

ICF elevations with openings, levels and roof build-up

SCALE	SIZE	DATE
1:200	A3	02.11.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-055-EL-01	-
