Delivery 1 - Load 1 of 2 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 269 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

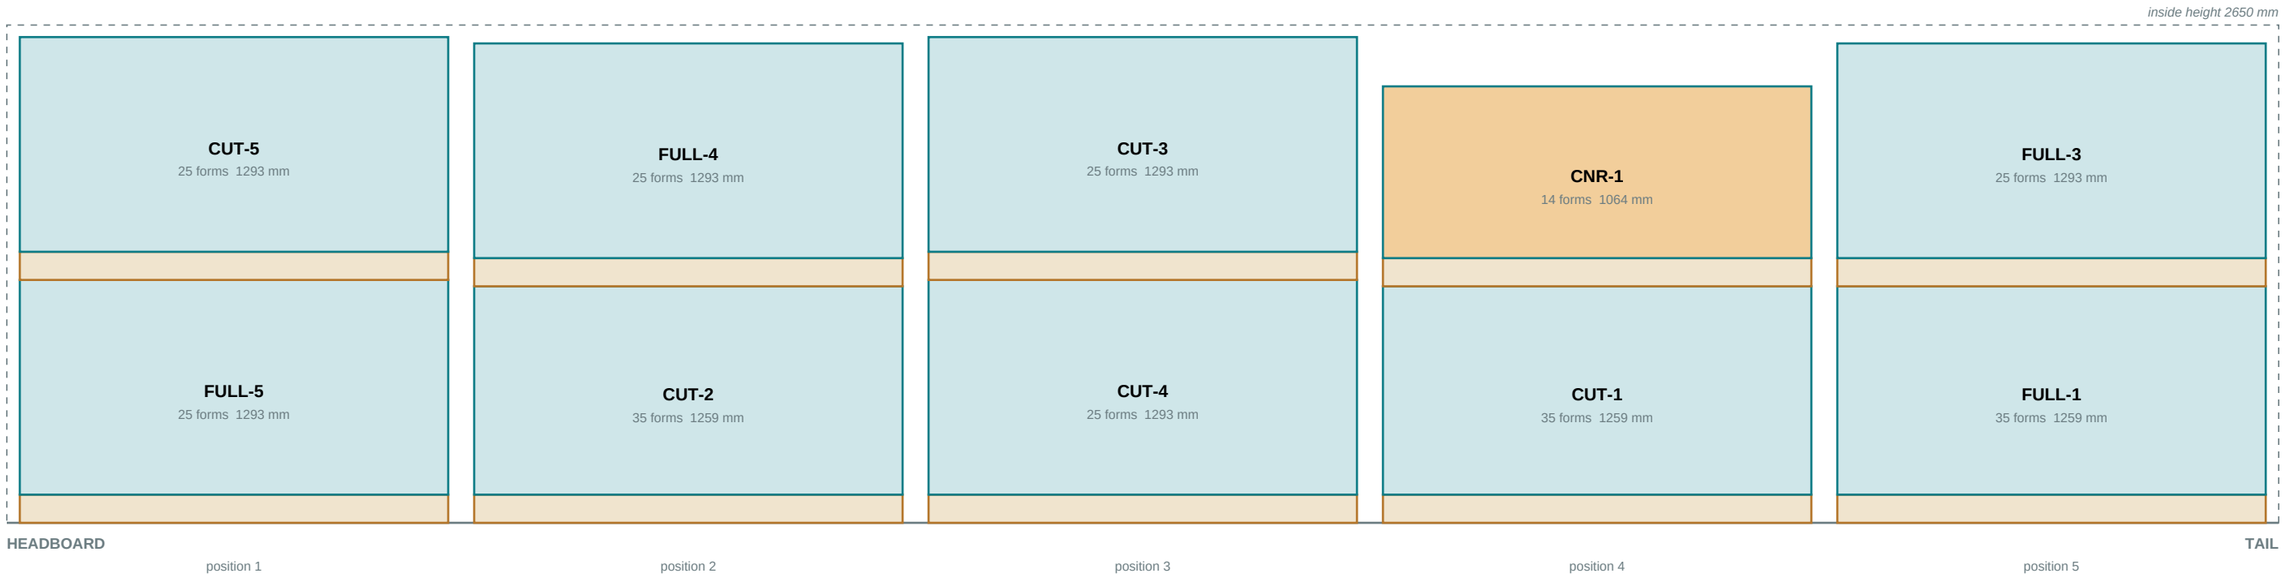

Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward

1. FULL-3 6in XR35 straights 25 forms courses L1 courses 1-3
2. FULL-1 6in Std straights 35 forms courses L1 courses 1-6
3. CNR-1 6in XR35 corners 14 forms courses L1 courses 1-7
4. CUT-1 6in Std straights 35 forms courses L1 courses 1-7
5. CUT-3 6in XR35 straights 25 forms courses L1 courses 1, 2, 3, 4, 6, 7
6. CUT-4 6in XR35 straights 25 forms courses L1 courses 2-7
7. FULL-4 6in XR35 straights 25 forms courses L1 courses 3-5
8. CUT-2 6in Std straights 35 forms courses L1 courses 4-7
9. CUT-5 6in XR35 straights 25 forms courses L1 courses 4, 5, 7
10. FULL-5 6in XR35 straights 25 forms courses L1 courses 5-7

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-055 Insubloc - 2 Castle Gardens, Swan…	FORMS	269
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	10	TALLEST	2586 mm

Delivery 1 - Load 2 of 2 - Artic 13.6 m

2 pallets in 1 of 5 floor positions | 26 forms | tallest column 1601 mm of 2650 mm inside height

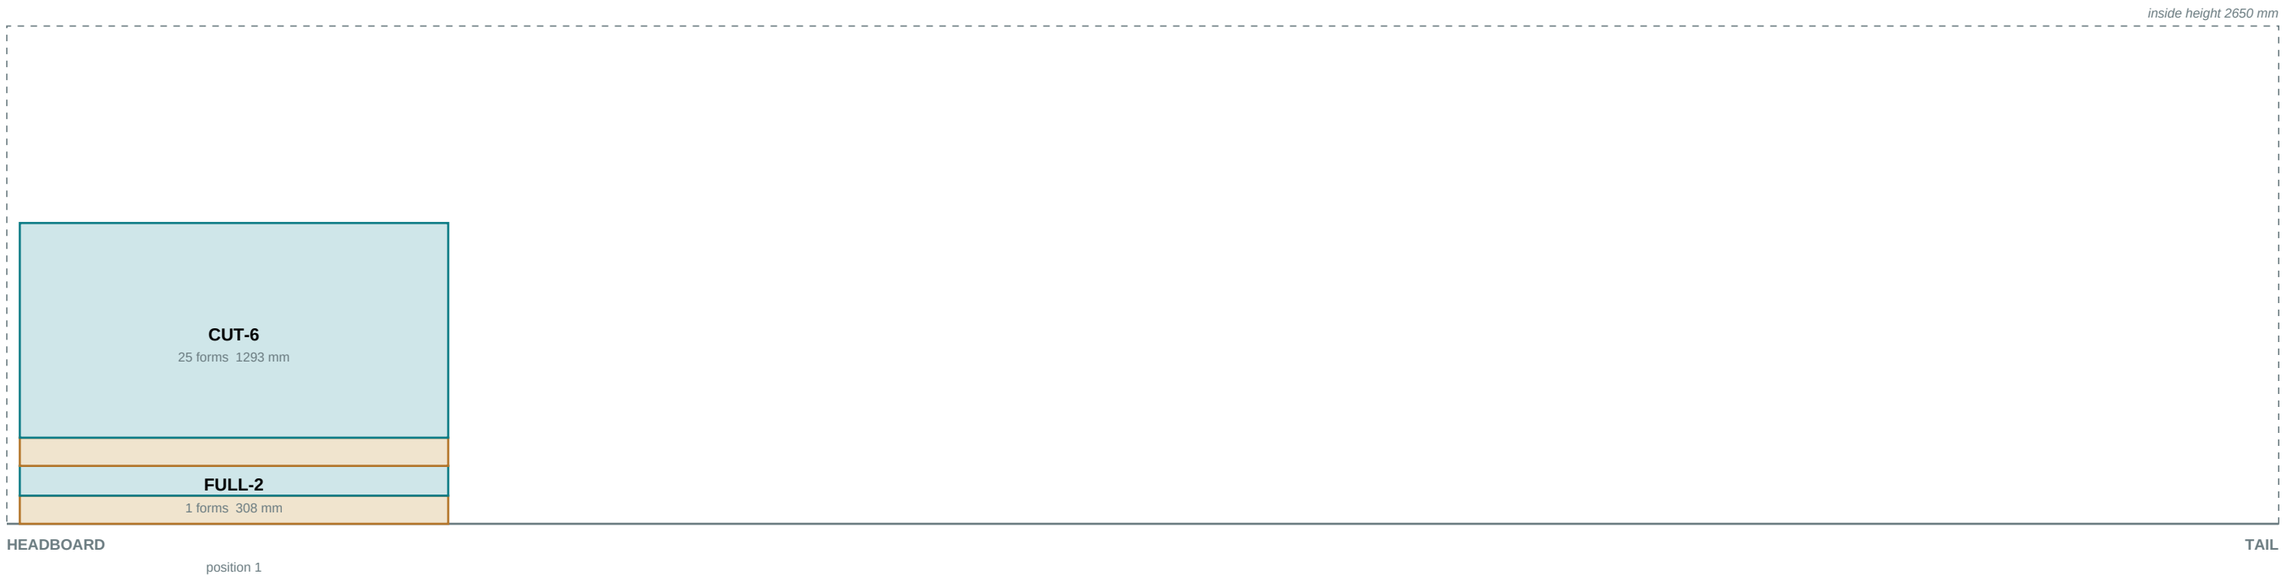

Unload order - 1 of 1 pallets come off out of build order, the price of stacking tallest forward

1. CUT-6 6in XR35 straights 25 forms courses L1 courses 6-7
2. FULL-2 6in Std straights 1 forms courses L1 course 7

Nudura™

WAGON STACKING PLAN

D1 LOAD 2

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-055 Insubloc - 2 Castle Gardens, Swan…	FORMS	26
VEHICLE	Artic 13.6 m	POSITIONS	1 of 5
PALLETS	2	TALLEST	1601 mm
