
SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura ICF to the new fourth-floor storey only - 6in XR35 external walls + 6in Standard stair-core and separating walls, 7 courses on the steel ring beam - pre-cut by BuildEase, stock forms and accessories by the distributor. The existing building, steelwork, floor, roof, partitions and finishes are shown or assumed in good faith only and must be checked by the relevant professional; the structural engineer to design the ring beam, transfer steels and the walls.


QUOTATION - NOT FOR CONSTRUCTION

J1 - 5,042 O/A x 253 - 57 No. (4F: FA1, FB1, FT1)




HUNG BOTH ENDS
left: RB1 UB 254 (E)
right: TB4 / TB5 / TB6 UB 406

J2 - 4,889 O/A x 253 - 46 No. (roof: RA1, RB1)




TOP-HUNG BOTH ENDS
left: ledger, E wall
right: ledger, separating wall

J3 - 4,764 O/A x 253 - 57 No. (4F: FA2, FB2, FT2)




HUNG BOTH ENDS
left: TB4 / TB5 / TB6 UB 406
right: RB2 UB 254 (W)

J4 - 4,611 O/A x 253 - 46 No. (roof: RA2, RB2)




TOP-HUNG BOTH ENDS
left: ledger, separating wall
right: ledger, W wall

J5 - 2,252 O/A x 253 - 25 No. (roof: RT)




HUNG off the EB1 edge beam (packer + face-fix hanger), TOP-HUNG
left: EB1 UB 254 edge beam
right: front-wall ledger

Elevations 1:25 along the span (left = east end for E-W joists, terrace edge for RT). Supports shown for context: UB steel end-on + C24 packer + hanger, or ICF wall + 47x178 ledger.

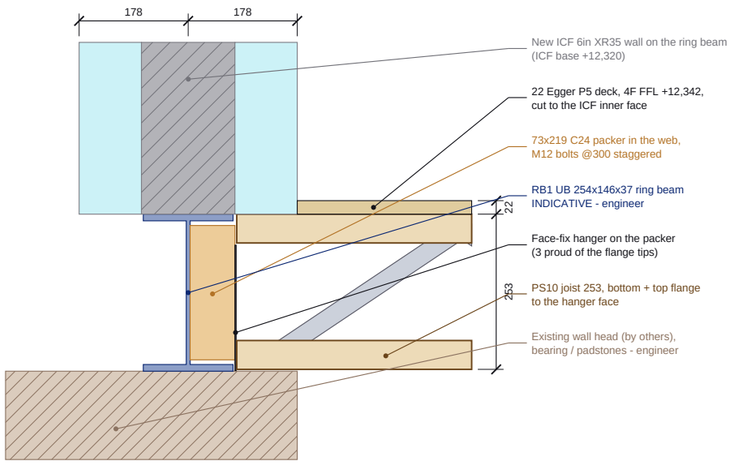

A HUNG END ON THE RING BEAM

Scale 1:10 | 4F, east side (RB1); TB / RB2 the same

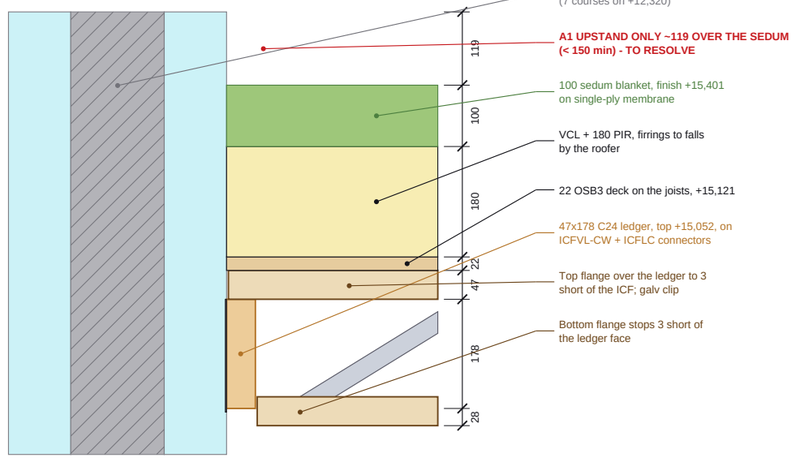

B TOP-HUNG ROOF END + BUILD-UP

Scale 1:10 | roof, east ICF wall; all ICF faces the same

JOIST TYPES AND STEELS

JOIST SCHEDULE (253 DEEP, 97X47 FLANGES)

Type	O/A	Bottom	Bearing	4F	Roof	Qty
J1	5,042	5,042	hung both ends	57	0	57
J2	4,889	4,795	top-hung both ends	0	46	46
J3	4,764	4,764	hung both ends	57	0	57
J4	4,611	4,517	top-hung both ends	0	46	46
J5	2,252	2,205	hung + top-hung	0	25	25
			Total	**114**	**117**	**231**

Qty includes the doubled (bolted) terrace-edge pairs. Layouts on ES26-055-FL-01 (4F) and ES26-055-RF-01 (roof).

WHERE USED (BAYS)

Type	Bays
J1	FA1, FB1, FT1
J2	RA1, RB1
J3	FA2, FB2, FT2
J4	RA2, RB2
J5	RT

STEEL SCHEDULE (INDICATIVE - ENGINEER)

Mark	Section	Line	Length	kg	Note
RB1	UB254x146x37	X 178	24,858	920	Ring beam, E side wall head
RB2	UB254x146x37	X 10,331	24,858	920	Ring beam, W (neighbour) wall head
RB3	UB254x146x37	Y 24,680	10,007	370	Ring beam, rear wall head
TB1	UB406x178x60	Y 2,585	10,007	601	Transfer, 4F front (terrace) wall
TB2	UB406x178x60	Y 11,886	10,007	601	Transfer, stair-core wall A
TB3	UB406x178x60	Y 15,346	10,007	601	Transfer, stair-core wall B
TB4	UB406x178x60	X 5,394	9,124	548	Transfer, separating wall A
TB5	UB406x178x60	X 5,394	9,172	551	Transfer, separating wall B
TB6	UB406x178x60	X 5,394	2,496	150	Terrace floor transfer (sep. line)
EB1	UB254x146x37	Y 73	9,998	370	Terrace roof edge beam (pockets)
	Total (indicative)			**5,633**	**S355**

Line = axis + centre (X along the building from the terrace edge, Y across from the east face). Ring beams + floor transfers top +12,320 (= ICF base); EB1 top +15,099. Packers per note 3.

NOTES

1. FOR SUPPLIER QUOTE: 253 deep metal-web joists, e.g. Posi-Joist / Easi-Joist PS10 equivalent, 97x47 C24 (or stress-graded) flanges with galvanised V-web plates @400 c/c. The supplier designs the joists for the stated loads and confirms depth, web layout, hangers, strongbacks and bracing.
2. Loads (to be confirmed by the supplier / engineer): 4F flats domestic 1.5 kN/m2 + stud partitions; covered terrace as a balcony / terrace loading; roof = 22 OSB3 + 180 PIR + membrane + 100 sedum (saturated) + snow + maintenance access. Plasterboard ceilings under.
3. Hung ends: face-fix joist hangers on C24 timber packers in the steel web (73 x 219 in the UB254, 88 x 360 in the UB406), packers 3 proud of the flange tips, M12 bolts @300 staggered. Never top-flange hangers on the steel.
4. Top-hung ends: top flange over the 47x178 ledger to 3 short of the ICF face, bottom flange 3 short of the ledger; galv restraint clip to the ledger. Web pattern indicative (quotation model).
5. STEELS INDICATIVE - the structural engineer designs the sections, bearings / padstones on the existing walls, connections, fire protection and the ICF pockets for EB1.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
Insubloc (distributor) - Tim Evans	2 Castle Gardens, Swansea - new fourth-floor storey (4 flats)

DRAWING TITLE
JOIST PROFILES AND STEEL SCHEDULE
Metal-web joist profiles for supplier quotation, bearing details, steel schedule

SCALE	SIZE	DATE
1:25 / 1:10	A3	02.11.26
DRAWN	**CHECKED**	**APPROVED**
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-055-FL-02	-

Do not scale. All dimensions in mm. Check all dimensions on site.
