
SUPPLY SCOPE (distributor quantities issue, no material prices): Nudura ICF to the new fourth-floor storey only - 6in XR35 external walls + 6in Standard stair-core and separating walls, 7 courses on the steel ring beam - pre-cut by BuildEase, stock forms and accessories by the distributor. The existing building, steelwork, floor, roof, partitions and finishes are shown or assumed in good faith only and must be checked by the relevant professional; the structural engineer to design the ring beam, transfer steels and the walls.

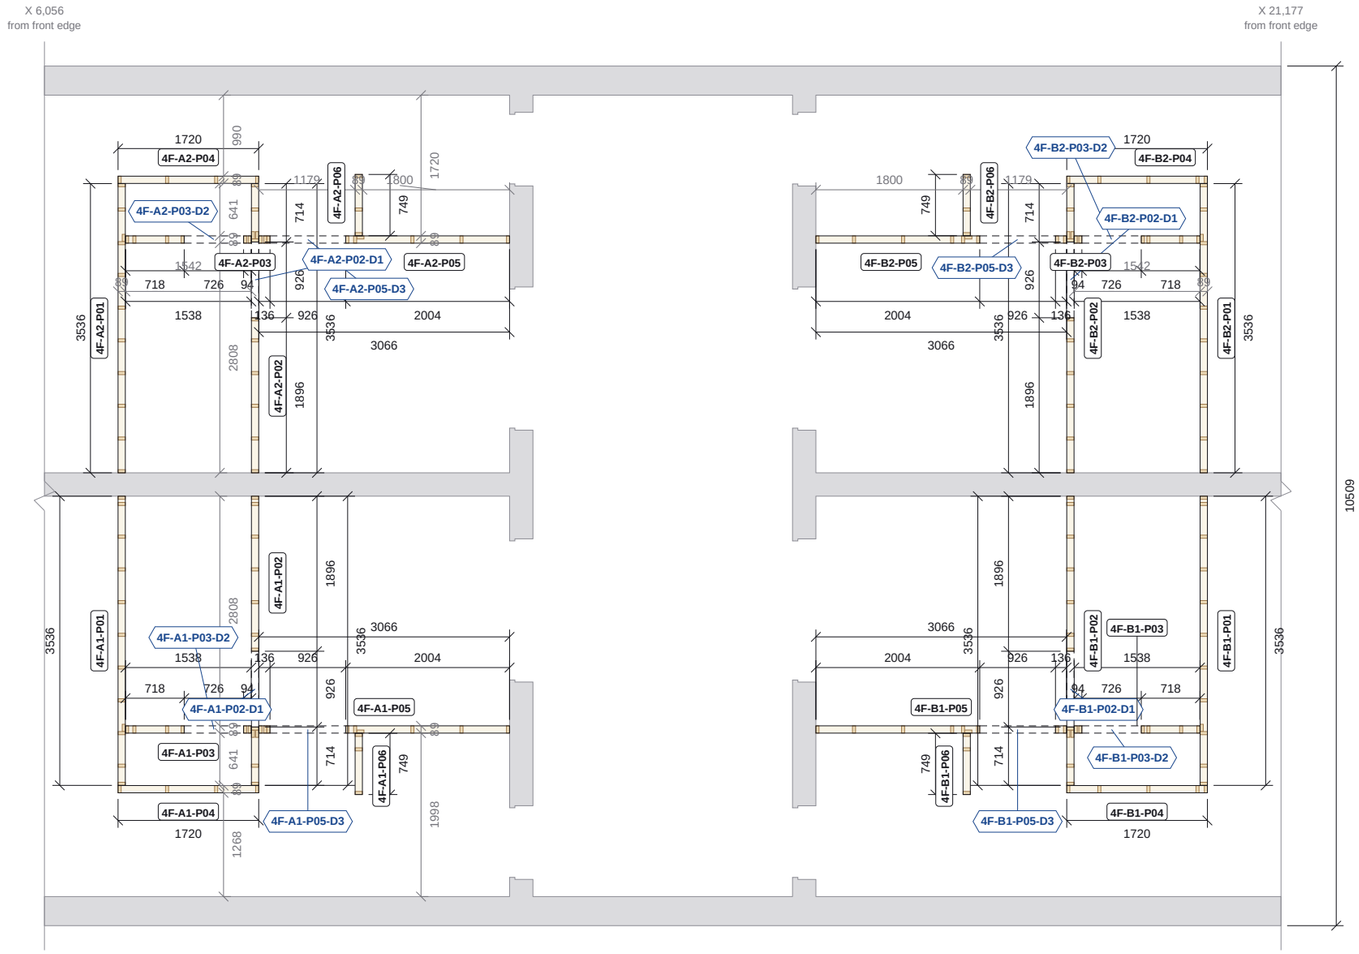

FOURTH FLOOR TIMBER PARTITIONS PLAN

Scale 1:75 @ A3 | Plan cut at 1200 above 4F FFL - view cropped to the partition zone, ICF overall on ES26-055-GA-01

0 1 2 3 4 5m

Partition panel, studs cut at plan level | Panel joint | Nudura ICF shell (context only) | Door opening, head over

PARTITION TIMBER (FOURTH FLOOR)

Section	Pieces	Run m	4.8m lengths
38x89 C16	440	618.4	136
47x97 C24 ceiling noggin	64	-	-
18 WBP ply pattress	116	-	-
Slotted partition head clip	128	-	-

From the model. 4.8m lengths = run / 4.8 +5%, not cut-optimised.

QUOTATION - NOT FOR CONSTRUCTION

FOURTH FLOOR SCHEDULES

PARTITION SCHEDULE

Panel	Head	C16 studs	Use	Length	Doors
4F-A1-P01	14,841	38x89 @400	wet room	3536	-
4F-A1-P02	14,841	38x89 @400	wet room	3536	4F-A1-P02-D1
4F-A1-P03	14,841	38x89 @400	wet room	1538	4F-A1-P03-D2
4F-A1-P04	14,841	38x89 @600	partition	1720	-
4F-A1-P05	14,841	38x89 @600	partition	3066	4F-A1-P05-D3
4F-A1-P06	14,841	38x89 @600	partition	749	-
4F-A2-P01	14,841	38x89 @400	wet room	3536	-
4F-A2-P02	14,841	38x89 @400	wet room	3536	4F-A2-P02-D1
4F-A2-P03	14,841	38x89 @400	wet room	1538	4F-A2-P03-D2
4F-A2-P04	14,841	38x89 @600	partition	1720	-
4F-A2-P05	14,841	38x89 @600	partition	3066	4F-A2-P05-D3
4F-A2-P06	14,841	38x89 @600	partition	749	-
4F-B1-P01	14,841	38x89 @400	wet room	3536	-
4F-B1-P02	14,841	38x89 @400	wet room	3536	4F-B1-P02-D1
4F-B1-P03	14,841	38x89 @400	wet room	1538	4F-B1-P03-D2
4F-B1-P04	14,841	38x89 @600	partition	1720	-
4F-B1-P05	14,841	38x89 @600	partition	3066	4F-B1-P05-D3
4F-B1-P06	14,841	38x89 @600	partition	749	-
4F-B2-P01	14,841	38x89 @400	wet room	3536	-
4F-B2-P02	14,841	38x89 @400	wet room	3536	4F-B2-P02-D1
4F-B2-P03	14,841	38x89 @400	wet room	1538	4F-B2-P03-D2
4F-B2-P04	14,841	38x89 @600	partition	1720	-
4F-B2-P05	14,841	38x89 @600	partition	3066	4F-B2-P05-D3
4F-B2-P06	14,841	38x89 @600	partition	749	-

Length along the wall (mm). Head = top of frame (model datum 0 = rear yard ground), 5 under the roof PS10 joist bottom chord +14,846.

DOOR OPENING SCHEDULE

Label	Width	Height	Head
4F-A1-P02-D1	926	2100	2100
4F-A1-P03-D2	726	2100	2100
4F-A1-P05-D3	926	2100	2100
4F-A2-P02-D1	926	2100	2100
4F-A2-P03-D2	726	2100	2100
4F-A2-P05-D3	926	2100	2100

Label	Width	Height	Head
4F-B1-P02-D1	926	2100	2100
4F-B1-P03-D2	726	2100	2100
4F-B1-P05-D3	926	2100	2100
4F-B2-P02-D1	926	2100	2100
4F-B2-P03-D2	726	2100	2100
4F-B2-P05-D3	926	2100	2100

Structural opening sizes. Head level above underside of the bottom rail.

NOTES

1. Non-load-bearing internal partitions (TLSTF): 38x89 C16 studs @600, 38x89 head and bottom rails, 15 plasterboard each side (119); shower-room walls (4 No. shower rooms) at 400 centres with 18 WBP ply pattress in the stud bays on the wet-room face, 150-1950 above floor (116 pieces).
2. DESIGN ASSUMPTION: partitions + doors read off planning drawing HG-24-02-05 rev 03 (planning) 1:100 - confirm against the architect's construction layout before order. ICF (grey: 6in XR35 external, 6in Std core / separating) context only; set-out strings (grey) from the ICF faces.
3. Non-load-bearing: heads stop 5 short of the flat-roof PS10 metal-web joist underside (bottom chord +14,846; frame top +14,841), restrained with galv slotted partition head clips to the joist bottom chords / 47x97 C24 ceiling noggins between chords (128 No. clips, 64 noggins where a partition runs parallel to the joists, 5 mm deflection gap) - clip product to confirm. Roof joists on ES26-055-RF-01 (joist designer to confirm).
4. Base = 4F FFL +12,342. Sole plates fixed through the 22 Egger Protect P5 deck to the PS10 floor joists / noggins at <= 600 c/c (hung 4F floor). Door openings are structural opening sizes. Dimensions to timber frame faces; check all dimensions on site.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
Insubloc (distributor) - Tim Evans	2 Castle Gardens, Swansea - new fourth-floor storey (4 flats)

DRAWING TITLE

FOURTH FLOOR TIMBER PARTITIONS

Internal stud partitions, panels and door openings

SCALE	SIZE	DATE
1:75	A3	02.11.26
DRAWN	CHECKED	APPROVED
TS		
STATUS	DRAWING No.	REV
QUOTATION	ES26-055-TF-01	-

Do not scale. All dimensions in mm. Check all dimensions on site.
