# Delivery 1 - Load 1 of 2 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 269 forms | tallest column 2586 mm of 2650 mm inside height

**Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.**

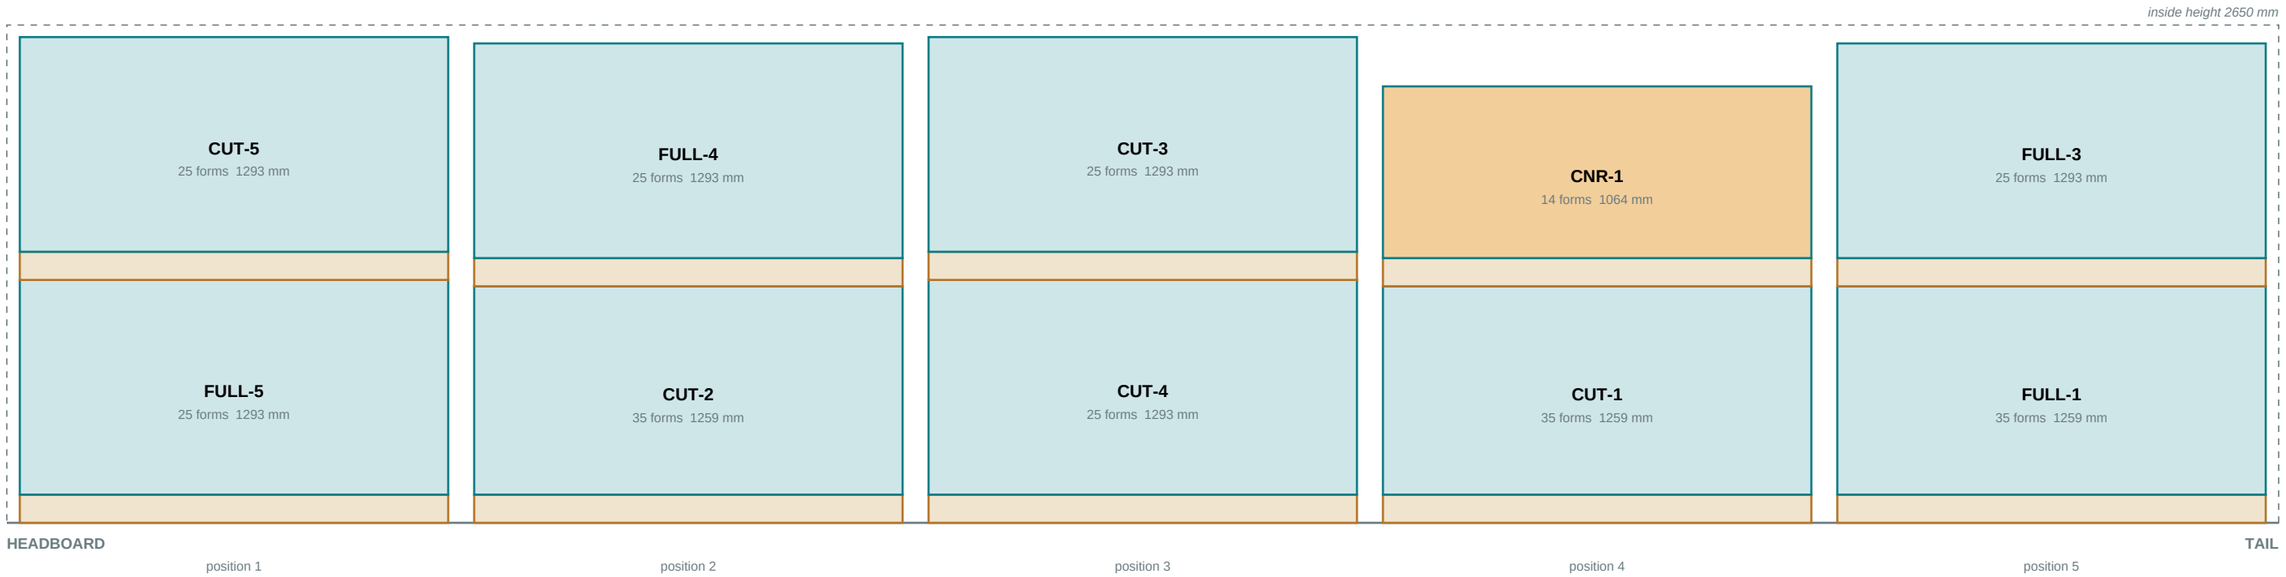


**Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward**

1. FULL-3 6in XR35 straights 25 forms courses L1 courses 1-3
2. FULL-1 6in Std straights 35 forms courses L1 courses 1-6
3. CNR-1 6in XR35 corners 14 forms courses L1 courses 1-7
4. CUT-1 6in Std straights 35 forms courses L1 courses 1-7
5. CUT-3 6in XR35 straights 25 forms courses L1 courses 1-7
6. CUT-4 6in XR35 straights 25 forms courses L1 courses 2, 3, 4, 5, 7
7. FULL-4 6in XR35 straights 25 forms courses L1 courses 3-5
8. CUT-2 6in Std straights 35 forms courses L1 courses 4-7
9. CUT-5 6in XR35 straights 25 forms courses L1 courses 4-7
10. FULL-5 6in XR35 straights 25 forms courses L1 courses 5-7

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

*Tallest column at the headboard; last needed on the floor*

| | | | |
|---|---|---|---|
| PROJECT | ES26-055 Insubloc - 2 Castle Gardens, Swan… | FORMS | 269 |
| VEHICLE | Artic 13.6 m | POSITIONS | 5 of 5 |
| PALLETS | 10 | TALLEST | 2586 mm |

# Delivery 1 - Load 2 of 2  -  Artic 13.6 m

2 pallets in 1 of 5 floor positions  |  24 forms  |  tallest column 1601 mm of 2650 mm inside height

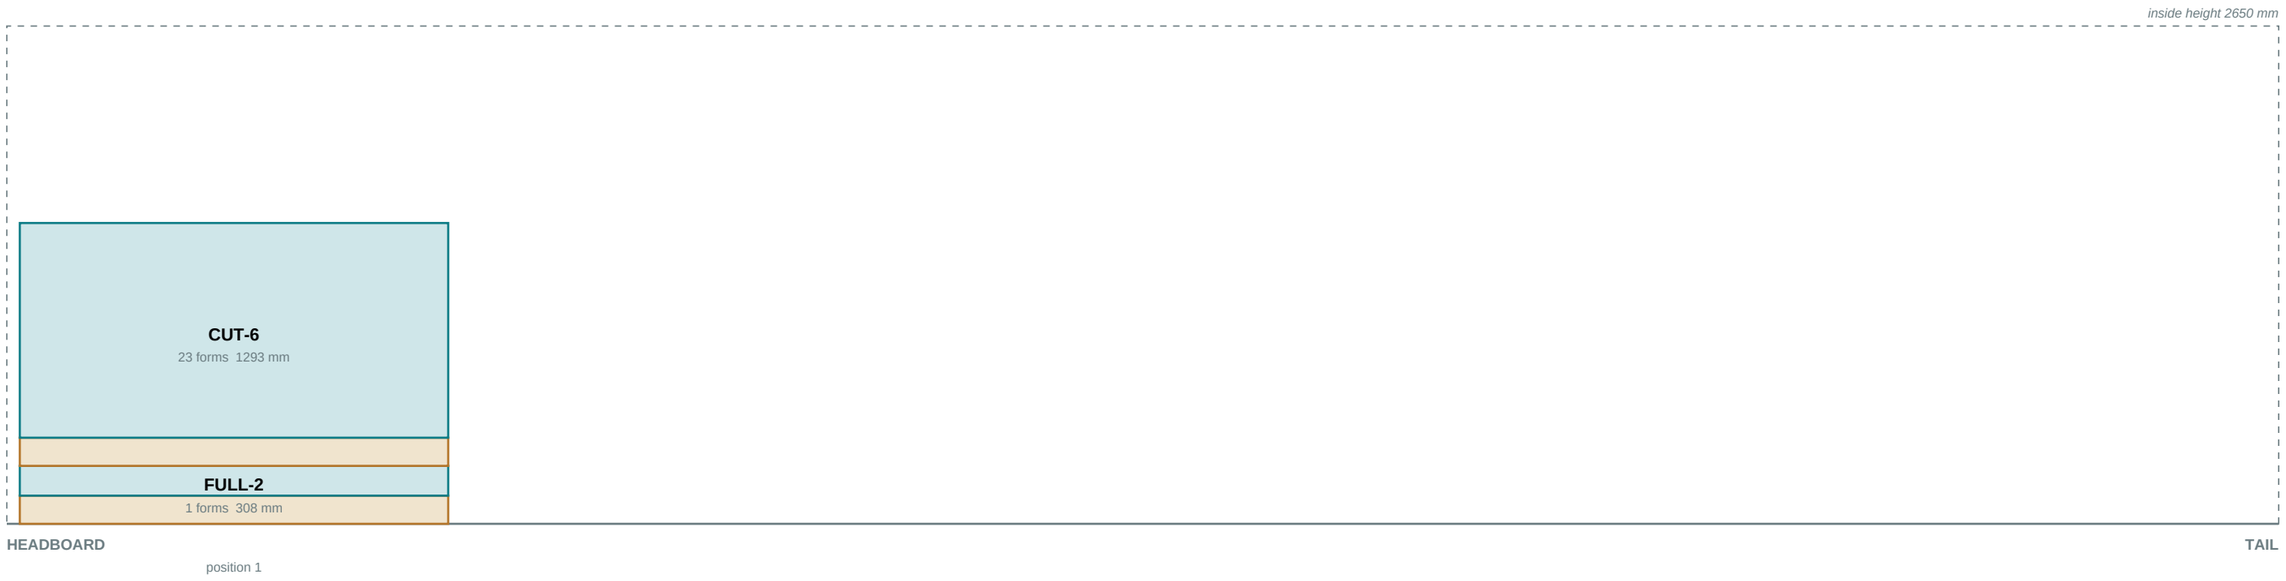


**Unload order - 1 of 1 pallets come off out of build order, the price of stacking tallest forward**

1. CUT-6  6in XR35 straights  23 forms  courses L1 courses 6-7
2. FULL-2  6in Std straights  1 forms  courses L1 course 7

Nudura™

**WAGON STACKING PLAN**

**D1 LOAD 2**

*Tallest column at the headboard; last needed on the floor*

| | | | |
|---|---|---|---|
| PROJECT | ES26-055 Insubloc - 2 Castle Gardens, Swan… | FORMS | 24 |
| VEHICLE | Artic 13.6 m | POSITIONS | 1 of 5 |
| PALLETS | 2 | TALLEST | 1601 mm |
